

Elementary Update Agenda



- Construction Progress Update
- Furniture Procurement
- Project Budget Tracking



Mineral Point Unified School District
11.9.20


Construction Progress Update

Progress during October 2020

- Continued installing rubber roofing
- Poured interior concrete floors
- Installing steel stud framing
- Installing mechanical rough-ins

Scheduled for November 2020

- Start installation of exterior windows and doors
- Start installation of Glu-lam structure at Mainstreet
- Continue mechanical rough-ins
- Continue steel stud framing

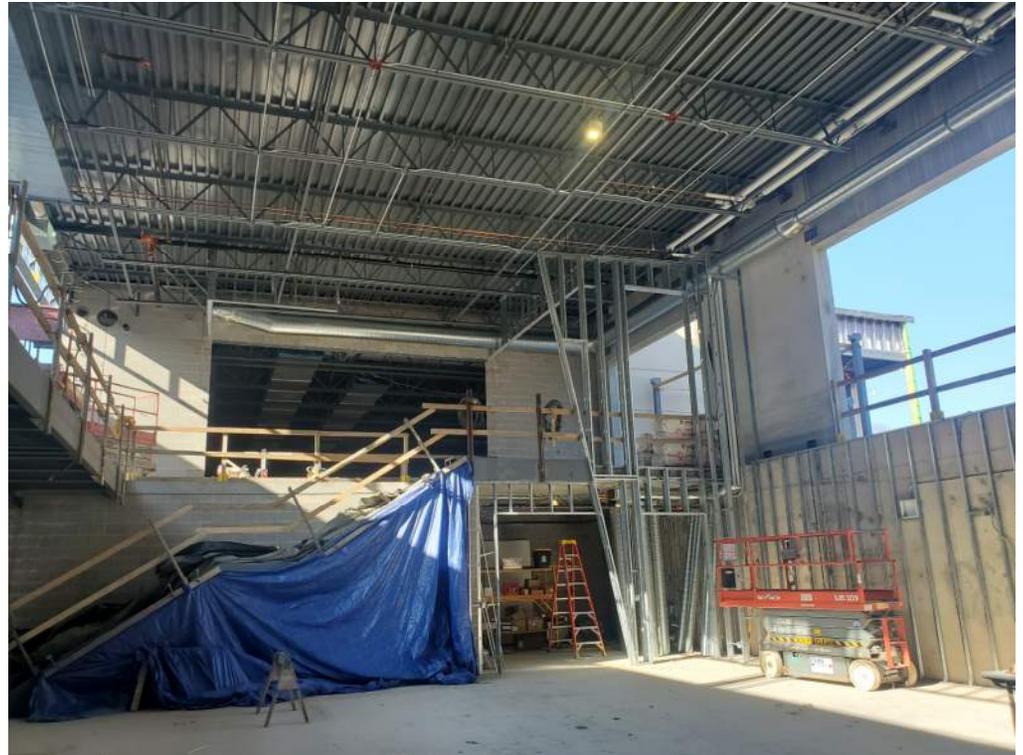


Library looking at north entry



Mineral Point Unified School District
11.9.20

Construction Progress Update

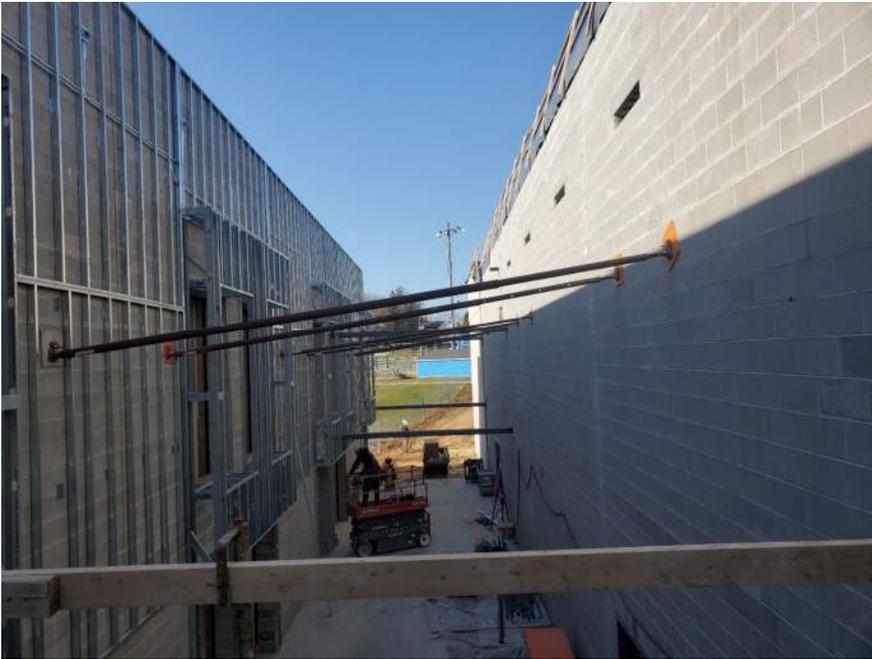

Main Street from Loft



Gym



Mineral Point Unified School District
11.9.20



Construction Progress Update



Wood Glu-lam over Main Street



Upper Loft Break Out Space



Mineral Point Unified School District
11.9.20



Construction Progress Update



Month 8 of 18
(44% Complete)

Phase 1:
Addition
Complete



Mineral Point Unified School District
11.9.20



Review Furniture Procurement Process



- Furniture vendor to work within an established budget (\$125,000)
- Furniture for new spaces (library and breakout spaces)
- Quality/ durability – touch and feel before ordering
- Coordinated design with furniture procurement.
- Samples/ example furniture


Vendors that submitted proposals:

- Lakeshore Learning
- Demo
- Alexander Furnishings
- Duet Resource Group



Mineral Point Unified School District
11.9.20



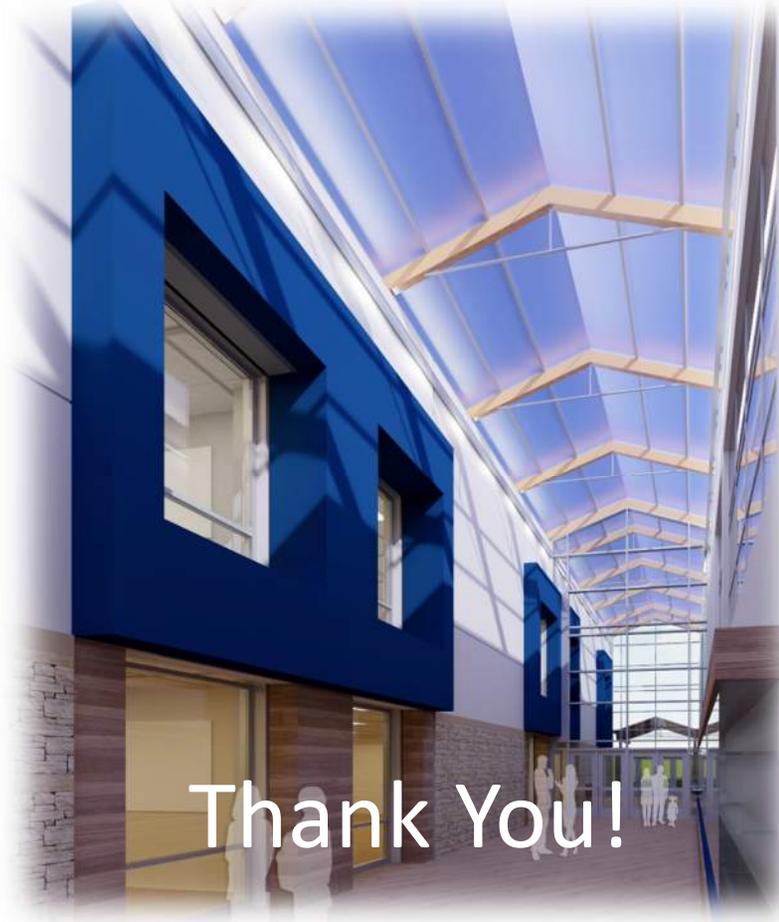

Thank You!

Mineral Point Unified School District
11.9.20

