Progress March/April:

- Start installation of Main StreetSkylight
- Installation of North Entry Canopy
- Start renovation of existing cafeteria/ gym
- Continue finishes in bathrooms off
 Main street
- Install stainless steel railing system







Overall Construction Schedule




March Month
13 of 18
(72% Complete)

May Phase 1:
Addition
Complete





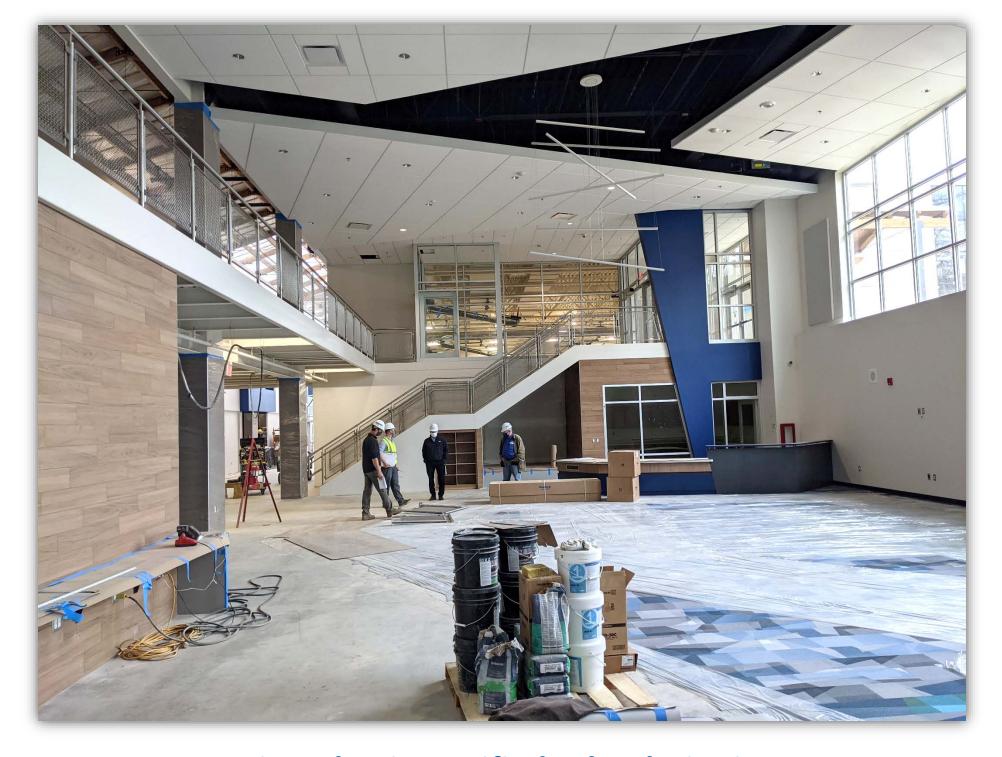








Main Street

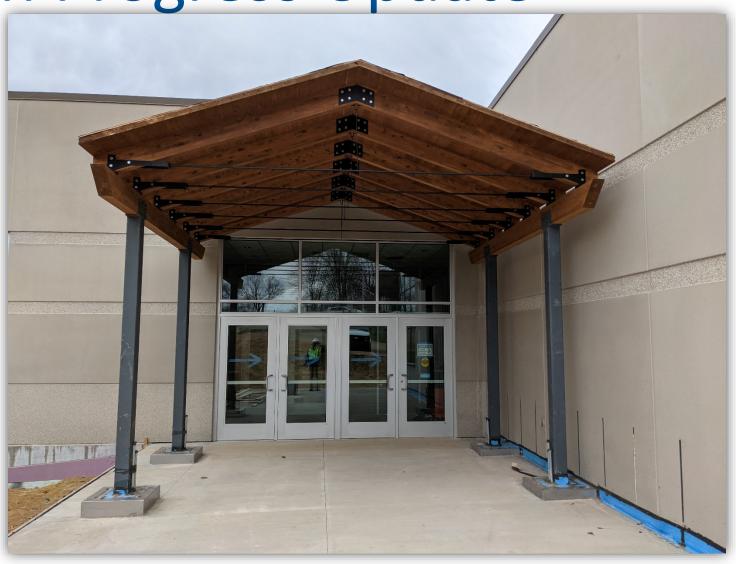

North Entry








Stainless Steel Railing



Restroom Tile





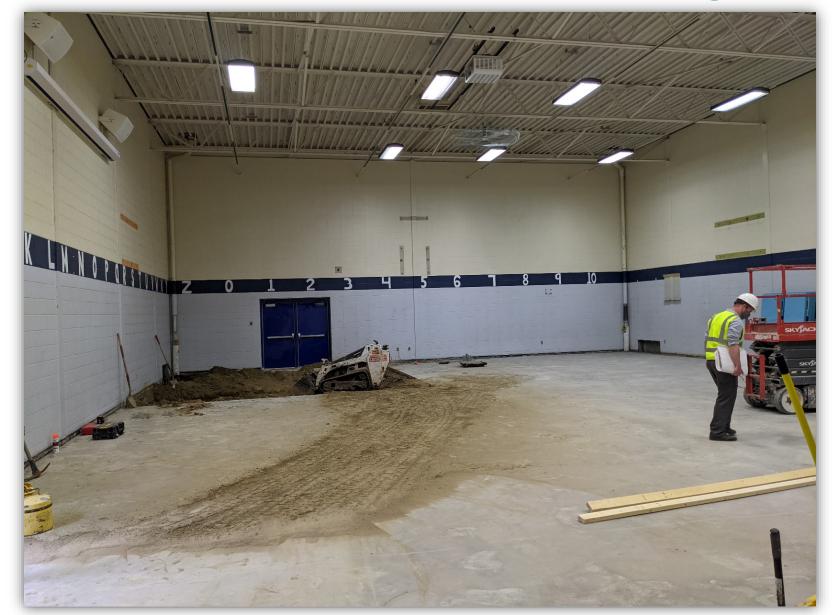




Plumbing camera scope of existing cast iron storm line under existing Cafeteria floor. Storm pipe needs to be replaced due to break in cast iron pipe. Believe it is a contributing factor to existing concrete slab heaving. Recommend replacement and routing overhead.







Demco Library Furniture Planning

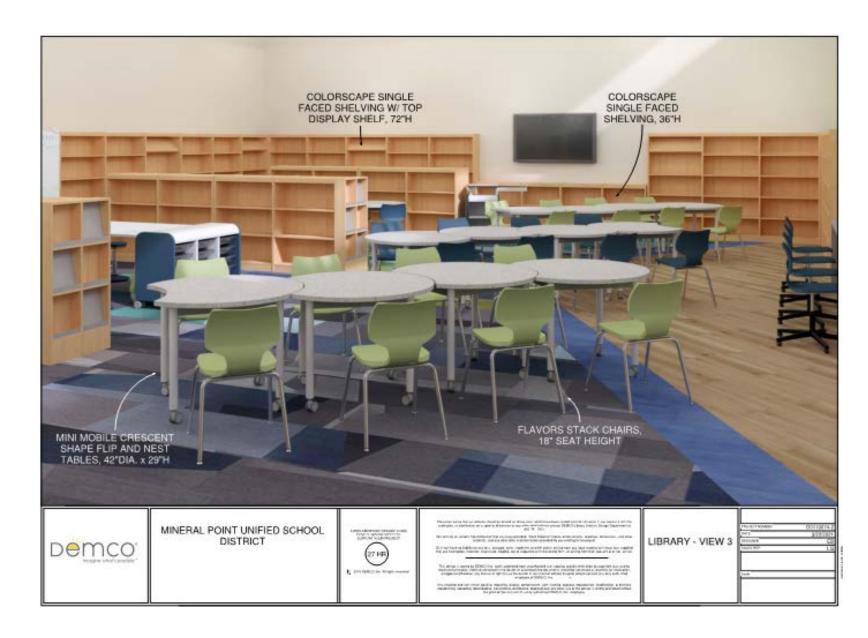









Added Restroom Finishes Alternate Pricing

Add \$72,425 for Alternate No. 5: Restroom Finishes Replacement in Boys 126, Girls 125, Boys 223, & Girls 222

This proposal provides a cost update to include applicable post-bid adjustments including inflation, independent small order fees, submittal coordination, and expediting. This pricing supersedes our original alternate pricing dated March 10, 2020, and updated pricing dated September 11, 2020.

Due to historic construction market volatility this proposal pricing is valid for 30 days.

Sincerely,

KRAEMER BROTHERS, LLC

Mitch Gilbertson Project Manager

