

Overall Construction Progress: Month 15 of 18 (83% Complete)

Overall Construction Schedule



Progress during May 2021

- Installed windows in Cafeteria
- Installed HVAC unit for Cafeteria
- Started site earthwork
- Started renovation of existing school

Scheduled for June 2021


- Remove concrete floor in lower level
- Start laying CMU and framing stud walls
- Start MEP rough-ins in renovation
- Start foundations for new front canopy



First Floor Demo Work

Mineral Point Unified School District
6.14.21



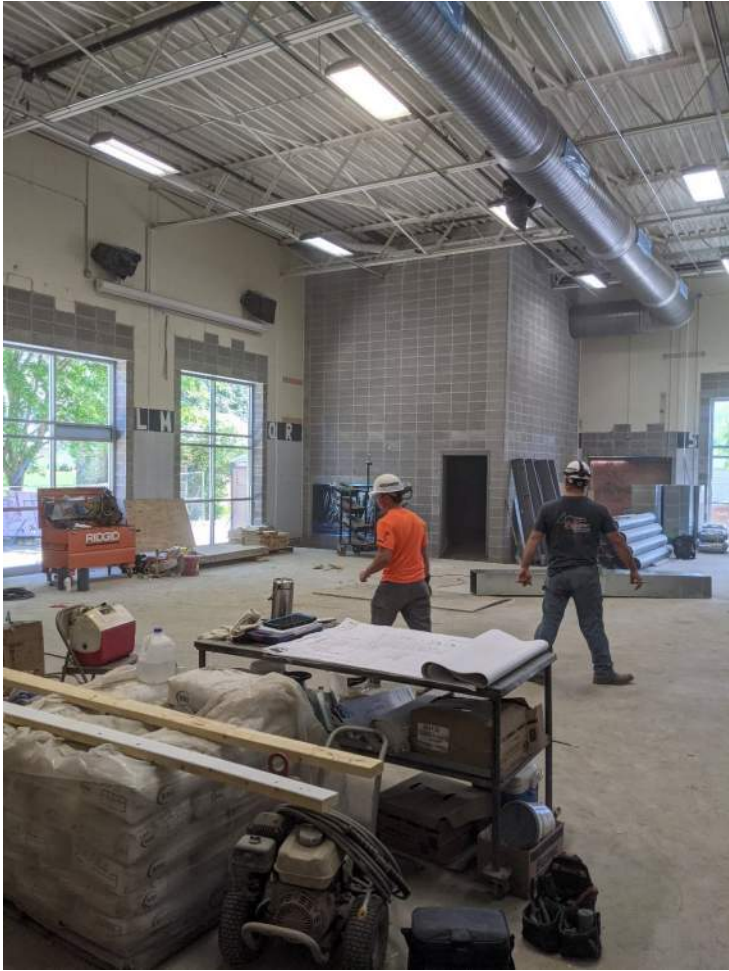


Mineral Point Unified School District
6.14.21



Mineral Point Unified School District
6.14.21



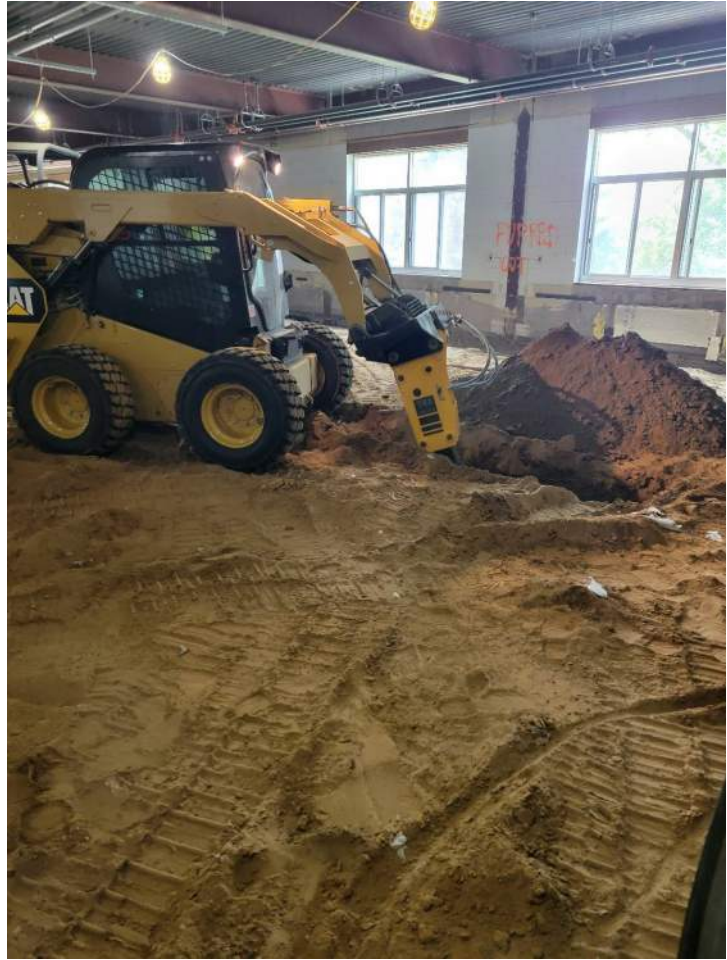

Mineral Point Unified School District
6.14.21


Overall Site



Mineral Point Unified School District
6.14.21



Site Traffic Flow

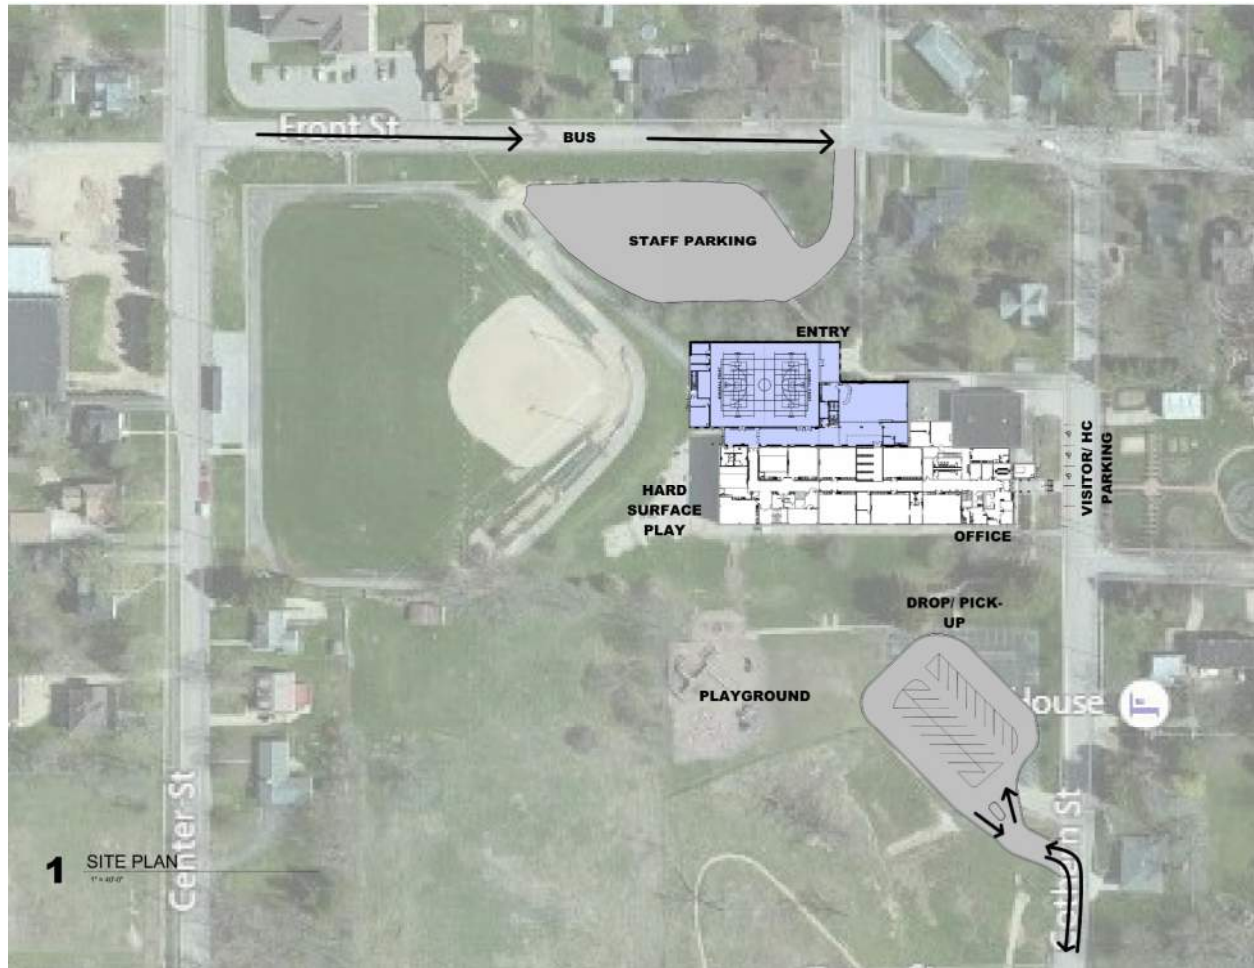

Mineral Point Unified School District
6.14.21





Thank You!



Mineral Point Unified School District
6.14.21

