

Construction Progress Update

Progress During January

- Install gym equipment
- Continue painting walls and ceilings
- Starting installing wall tile
- Installing mechanical/electrical finishes

Scheduled for February 2021

- Install wood gym wood flooring
- Continue painting walls and ceilings
- Continue install wall and floor finishes
- Continue installing wall tile and finishes



New Gym



Mineral Point Unified School District
2.08.21

Construction Progress Update



North Entry



Upper Main Street



Mineral Point Unified School District
2.08.21


Construction Progress Update



Gym Finishes



Electrical Room

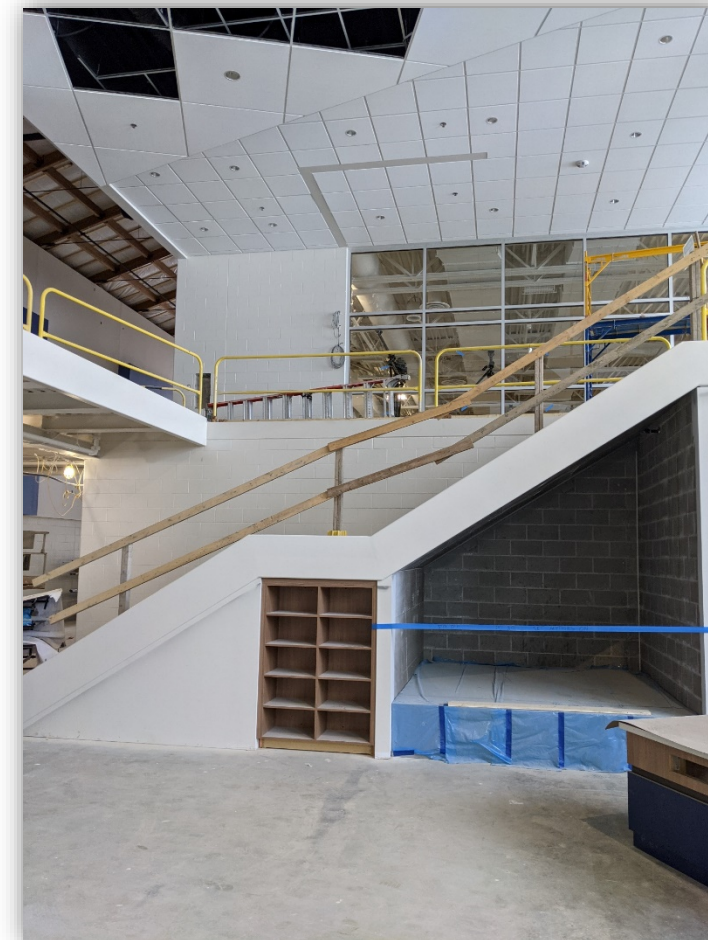

Library Nook



Mineral Point Unified School District
2.08.21

Construction Progress Update



Library



North Grand Stair



Mineral Point Unified School District
2.08.21



Construction Progress Update

Overall Construction Schedule



February Month
11 of 18
(61% Complete)

May Phase 1:
Addition
Complete



Mineral Point Unified School District
2.08.21





Thank You!



Mineral Point Unified School District
2.08.21
