



Project Update

December 2020

Overall Construction Schedule



Progress during November 2020

- Continued installation of exterior windows and doors
- Installed the glu-lam structure at Mainstreet
- Continued mechanical rough-ins
- Continued steel stud framing and started drywall installation

Scheduled for December 2020

- Continue drywall installation and finishing
- Start painting walls and ceilings
- Start installing ceiling tile grid-work
- Continue installing exterior windows and doors




North Entry



New Electrical Service



Main Street

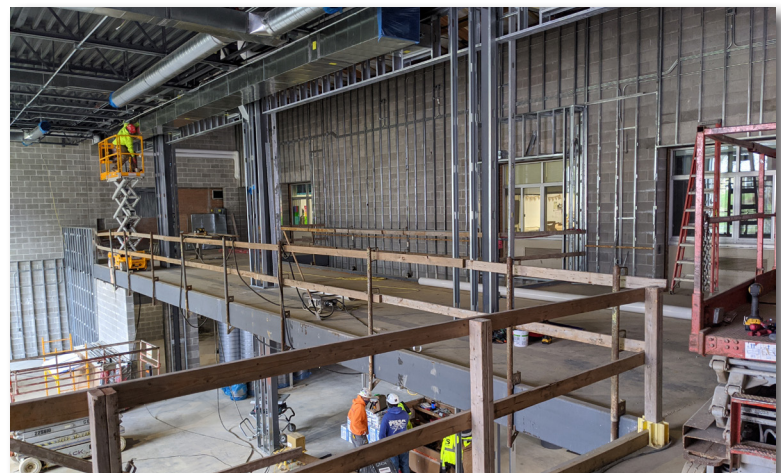

Loft
