



# Project Update

November 2020

## Overall Construction Schedule



## Progress during October 2020

- Continued installing rubber roofing
- Poured interior concrete floors
- Installing steel stud framing
- Installing mechanical rough-ins

## Scheduled for November 2020

- Start installation of exterior windows and doors
- Start installation of Glu-lam structure at Mainstreet
- Continue mechanical rough-ins
- Continue steel stud framing




North Entry Exterior



Library Looking Up



Interior Walkway

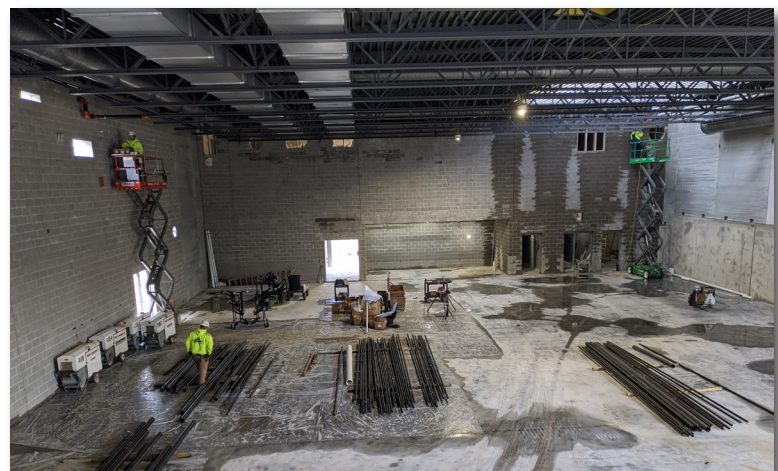

Gymnasium
